

# Commercial Centres Revitalisation Project Update #14 - September 2021

## Pinnaroo Village Green Project (PVGP)

Stage 1 project works are progressing well. Over the last fortnight the focus has been construction of new kerbing at the western end as well as installation of new stormwater and irrigation systems. Rubble preparation for the asphalt path at the western end is also well underway. In the coming weeks paving will begin on-site and more concreting and kerbing works will be completed.

The PVGMP Steering Committee has had a busy month with meetings held on both 2 August and 24 August. A huge thank you to our committee members for their continued commitment to the project. The concept design for Stages 2 & 3 has now been endorsed by the steering committee which is an exciting milestone for the project.

An overview of the proposed Eastern Entrance Project was also presented and discussed in the recent steering committee meeting including the plans for the entrance screen concept design.

## Lameroo Town Centre Plan (LTCP)

Fabrication of the centre pivot play equipment piece is now complete. The piece is awaiting painting after which an installation date is expected to be confirmed. The aim is to install the centre pivot piece, pavilion and picnic setting together which will be an exciting day for the project.

The pump track is still awaiting asphaltting which is scheduled to occur later this month. It will be great to open the pump track and see it being enjoyed by the community.

Birdseye Studios are continuing to progress the Stages 2 & 3 design considering the site footprint for the new community meeting space and how this will complement the surrounding amenities and leisure spaces.


## Commercial Centres Revitalisation Project Funding Update (CCRP)

Stage 1 of both commercial centre projects are funded by the Commonwealth Government Department of Industry, Innovation and Science (Commonwealth Drought Extension Programme).

Stages 2 and 3 are funded by the Commonwealth Government Department of Industry, Science, Energy and Resources (Building Better Regions).

## Project Communications

Visit the Southern Mallee District Council's Major Projects Website Page to stay up-to-date: <https://www.southernmallee.sa.gov.au/your-council/major-projects>

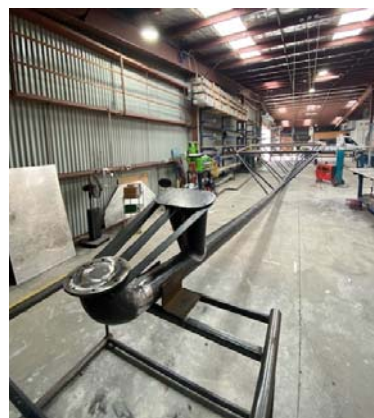

### PVGP SNAPSHOT

#### What's changed?

- The recent focus of Stage 1 works has been the installation of kerbing, stormwater and irrigation systems.
- The concept design for Stages 2 & 3 has been endorsed.

### LTCP SNAPSHOT

#### What's changed?

- Fabrication of the centre pivot play equipment piece is complete, now awaiting painting.

### FUNDING SNAPSHOT

#### Stage 1

- Funded by \$1m of Commonwealth Drought Funding.

#### Stage 2 & 3

- Funded by \$2.25m of Commonwealth Building Better Regions Funding.
- Council contribution of \$750,000.
